

Page 12 of 22

RR

End Autumn Semester Examination (2010-2011)
Dept. of Architecture & Regional Planning
Indian Institute of Technology Kharagpur

Sub. No: AR52001 Sub. Name : Construction Project Management
 Time : 3 hours Full Marks: 100


- 1 Write short notes on (any three): 5x3
 a. Precedence networking b. Risk estimation c. Slack
- 2 Compare 5x2
 a. CPM & PERT b. Rough & detailed estimate

- 3 A small project consists of 10 jobs as shown. Their duration (optimistic, most probable & pessimistic) and precedence relationship are given.
 a Draw network diagram using expected time of each job. Show critical path in it.
 b What is the probability that the project can be finished in 20 days and in 18 days?
 c If, uncertainties in the project are removed, probabilistic expected job times become deterministic. Prepare a chart for all jobs showing:
- Early start-early finish schedule
 - Total slack and free slack

Job	Immediate predecessor	Duration (weeks)		
		To	Tm	Tp
A	—	3	4	5
B	A	1	2	3
C	A	4	6	8
D	B	1	3	5
E	C	5	9	13
F	—	1	2	3
G	F	3	5	7
H	F	4	7	10
I	D,E,G	1	2	3
J	H	7	10	13

10+10
+10

- 4 Given is the network diagram of a project. If project deadline is 20 days, overhead cost is \$100/day and penalty for exceeding deadline is \$100/day, find the most profitable project duration. Crashed duration of A is 5 days means A can't be crashed beyond 5 days. Assume unlimited manpower. 15

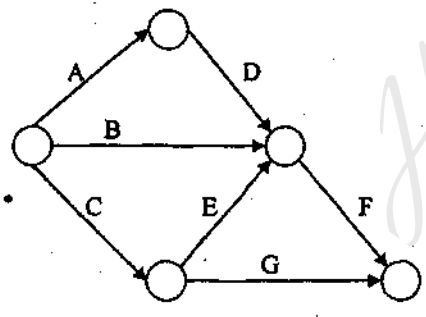


Job	Normal duration (days)	Crashed duration (days)	Crashing cost (\$/day)	Crew size
A	8	5	25	5
B	15	10	30	5
C	9	6	20	9
D	10	6	15	6
E	4	3	10	3
F	5	4	40	7
G	2	1	20	8

- 5 In Q.4., consider job time = crashed duration i.e. A,B,....,G take 5,10,...,1 days to complete. If there are 11 workers in the project team, apply heuristic method for resource allocation. What is the shortest project duration? Neglect all cost components. 15
- 6 a. Utilize your 3 weeks of winter vacation to convert your backyard into a nice sit-out area. Plan 10-12 activities with expected durations. Show them in a network diagram with critical path. 10+5
 b. What are the possible risk factors associated with this project?

Note: Z table and Graph sheets provided.

.....END.....

Standard Normal distribution (Area under the standard normal curve)

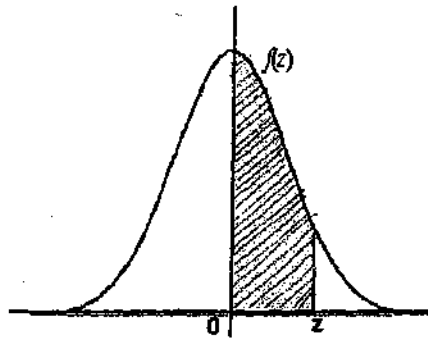

z	.00	.01	.02	.03	.04	.05	.06	.07	.08	.09
0.0	0.5000	0.5040	0.5080	0.5120	0.5160	0.5199	0.5239	0.5279	0.5319	0.5359
0.1	0.5398	0.5438	0.5478	0.5517	0.5557	0.5596	0.5636	0.5675	0.5714	0.5753
0.2	0.5793	0.5832	0.5871	0.5910	0.5948	0.5987	0.6026	0.6064	0.6103	0.6141
0.3	0.6179	0.6217	0.6255	0.6293	0.6331	0.6368	0.6406	0.6443	0.6480	0.6517
0.4	0.6554	0.6591	0.6628	0.6664	0.6700	0.6736	0.6772	0.6808	0.6844	0.6879
0.5	0.6915	0.6950	0.6985	0.7019	0.7054	0.7088	0.7123	0.7157	0.7190	0.7224
0.6	0.7257	0.7291	0.7324	0.7357	0.7389	0.7422	0.7454	0.7486	0.7517	0.7549
0.7	0.7580	0.7611	0.7642	0.7673	0.7704	0.7734	0.7764	0.7794	0.7823	0.7852
0.8	0.7881	0.7910	0.7939	0.7967	0.7995	0.8023	0.8051	0.8078	0.8106	0.8133
0.9	0.8159	0.8186	0.8212	0.8238	0.8264	0.8289	0.8315	0.8340	0.8365	0.8389
1.0	0.8413	0.8438	0.8461	0.8485	0.8508	0.8531	0.8554	0.8577	0.8599	0.8621
1.1	0.8643	0.8665	0.8686	0.8708	0.8729	0.8749	0.8770	0.8790	0.8810	0.8830
1.2	0.8849	0.8869	0.8888	0.8907	0.8925	0.8944	0.8962	0.8980	0.8997	0.9015
1.3	0.9032	0.9049	0.9066	0.9082	0.9099	0.9115	0.9131	0.9147	0.9162	0.9177
1.4	0.9192	0.9207	0.9222	0.9236	0.9251	0.9265	0.9279	0.9292	0.9306	0.9319
1.5	0.9332	0.9345	0.9357	0.9370	0.9382	0.9394	0.9406	0.9418	0.9429	0.9441
1.6	0.9452	0.9463	0.9474	0.9484	0.9495	0.9505	0.9515	0.9525	0.9535	0.9545
1.7	0.9554	0.9564	0.9573	0.9582	0.9591	0.9599	0.9608	0.9616	0.9625	0.9633
1.8	0.9641	0.9649	0.9656	0.9664	0.9671	0.9678	0.9686	0.9693	0.9699	0.9706
1.9	0.9713	0.9719	0.9726	0.9732	0.9738	0.9744	0.9750	0.9756	0.9761	0.9767
2.0	0.9772	0.9778	0.9783	0.9788	0.9793	0.9798	0.9803	0.9808	0.9812	0.9817
2.1	0.9821	0.9826	0.9830	0.9834	0.9838	0.9842	0.9846	0.9850	0.9854	0.9857
2.2	0.9861	0.9864	0.9868	0.9871	0.9875	0.9878	0.9881	0.9884	0.9887	0.9890
2.3	0.9893	0.9896	0.9898	0.9901	0.9904	0.9906	0.9909	0.9911	0.9913	0.9916
2.4	0.9918	0.9920	0.9922	0.9925	0.9927	0.9929	0.9931	0.9932	0.9934	0.9936
2.5	0.9938	0.9940	0.9941	0.9943	0.9945	0.9946	0.9948	0.9949	0.9951	0.9952
2.6	0.9953	0.9955	0.9956	0.9957	0.9959	0.9960	0.9961	0.9962	0.9963	0.9964
2.7	0.9965	0.9966	0.9967	0.9968	0.9969	0.9970	0.9971	0.9972	0.9973	0.9974
2.8	0.9974	0.9975	0.9976	0.9977	0.9977	0.9978	0.9979	0.9979	0.9980	0.9981
2.9	0.9981	0.9982	0.9982	0.9983	0.9984	0.9984	0.9985	0.9985	0.9986	0.9986
3.0	0.9987	0.9987	0.9987	0.9988	0.9988	0.9989	0.9989	0.9989	0.9990	0.9990
3.1	0.9990	0.9991	0.9991	0.9991	0.9992	0.9992	0.9992	0.9992	0.9993	0.9993
3.2	0.9993	0.9993	0.9994	0.9994	0.9994	0.9994	0.9994	0.9995	0.9995	0.9995
3.3	0.9995	0.9995	0.9995	0.9996	0.9996	0.9996	0.9996	0.9996	0.9996	0.9997
3.4	0.9997	0.9997	0.9997	0.9997	0.9997	0.9997	0.9997	0.9997	0.9997	0.9998

2x+2y=1
